



Operations Advisory Committee Meeting January 28th, 2021

Capital Planning and Projects Overview

Motorgate Garage Repairs

Contract Value: \$16,464,613.00

Total Approved Construction Change Orders: \$1,641,306.31

Percentage Complete: 85%

Projected Completion Date: April 2021

Contract Budget: \$20,419,393.36

Total Contingency Remaining: \$2,313,474.05

Status: Project proceeding as scheduled


Before




After




Motorgate Garage Repairs

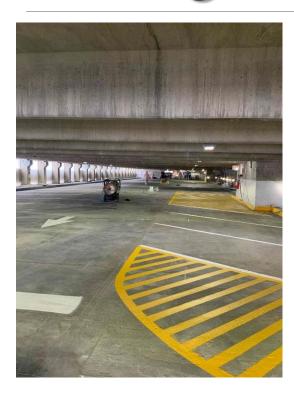

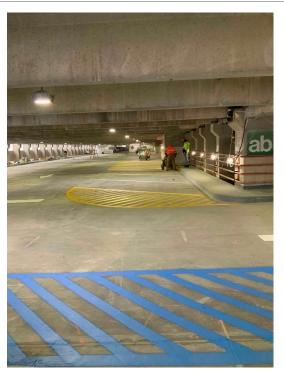



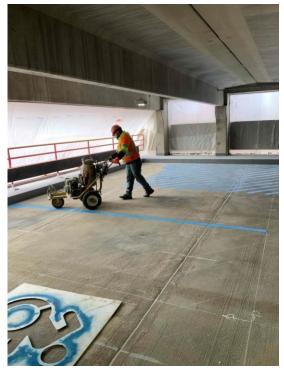

Southpoint Park Rip Rap Revetment


Contract Value: \$10,826,333.00

Total Approved Construction Change Orders: \$221,697.00

Percentage Complete: 47%

Project Completion Date: November 2021

Before

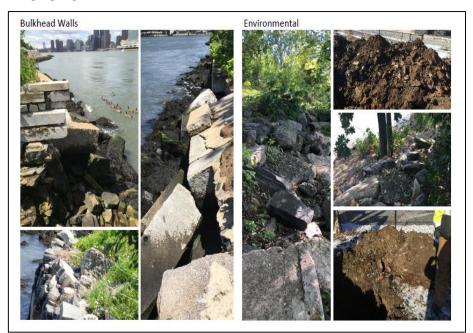

Contract Budget: \$12,991.599.60


Total Contingency Remaining: \$1,943,569.60


Status: Project proceeding as scheduled

Current



Southpoint Park Rip Rap Revetment

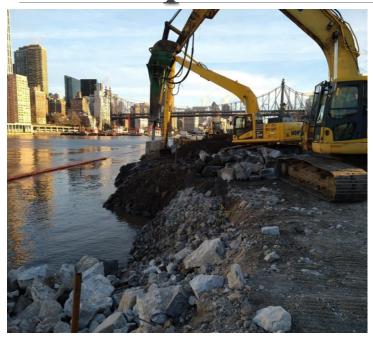

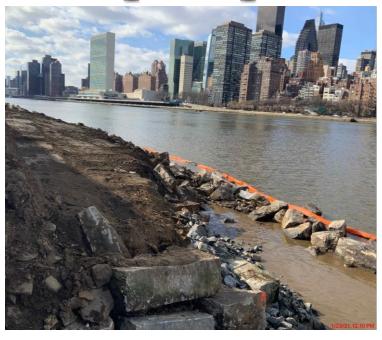



Southpoint Park



Youth Center Renovation

Contract Value: \$1,889,499.00

Total Approved Construction Change Orders: \$294,448.96

Status: Project completion pending FDNY re-inspection

Contract Budget: \$2,172,923.85

Percentage Complete: 99%

Before





After





Jack MacManus Field Comfort Station

Contract Value: \$5,172,085.00

Total Approved Construction Change Orders: \$131,453.49

Percentage Complete: 64%

Project Completion Date: June 2021(Seating Area will be open in Spring of 2021)

Before



Current



Contract Budget: \$ 5,923,545.35

Total Contingency Remaining: \$641,182.86


Status: Project proceeding as scheduled

Jack MacManus Field Comfort Station







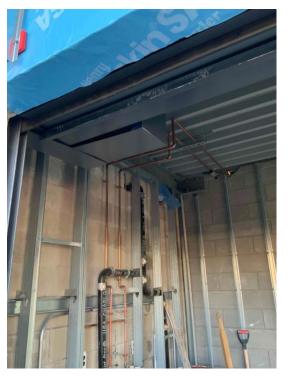

Jack MacManus Field Comfort Station





Hope Memorial

Contract Value: \$650,000.00

Total Approved Construction Change Orders: \$31,577.59

Percentage Complete: 99%

Project Completion Date: Project in closeout phase

Contract Budget: \$682,500.00

Total Contingency Remaining: \$922.41

Status: Project proceeding as scheduled

Before






Hope Memorial





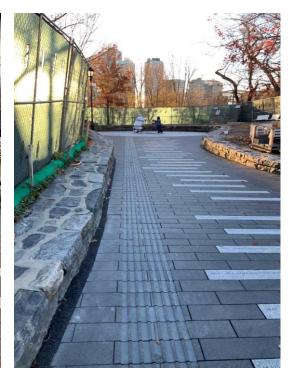



Tramway Elevator

Contract Value: \$5,580,000.00

Total Approved Construction Change Orders: \$1,297,115.30

Percentage Complete: 64%

Project Completion Date: Eastern Elevator Will Open in July 2021, Western Elevator will Open in December 2021

Before



Current



Contract Budget: \$7,090,641.13

Total Contingency Remaining: \$213,525.83

Status: Project proceeding as scheduled

Tramway Elevator







Tramway Elevator

